ID	Task Name	Duration	Start	Finish	Predecessors
1	Mobilization & Site Hoarding	1 day?	Mon 18/05/15	Mon 18/05/15	
2	Demotlion & Removals	2 days	Tue 19/05/15	Wed 20/05/15	1
3	Excavation	2 days	Thu 21/05/15	Fri 22/05/15	2
4	Splash Pad Installation	5 days	Mon 25/05/15	Fri 29/05/15	3
5	Shade Toppers Footing	2 days	Mon 01/06/15	Tue 02/06/15	4
6	Fence post footings	2 days	Wed 03/06/15	Thu 04/06/15	5
7	Concrete Work	6 days	Fri 05/06/15	Fri 12/06/15	6
8	Site Furnitire	1 day?	Mon 15/06/15	Mon 15/06/15	7
9	Restoration & Sodding	1 day?	Tue 16/06/15	Tue 16/06/15	8
10	28 day lead time for colour surface	20 days	Thu 11/06/15	Wed 08/07/15	
11	Colour Surfacing	5 days	Wed 08/07/15	Tue 14/07/15	
12	Hoarding Removal & Final cleanup	1 day?	Fri 17/07/15	Fri 17/07/15	

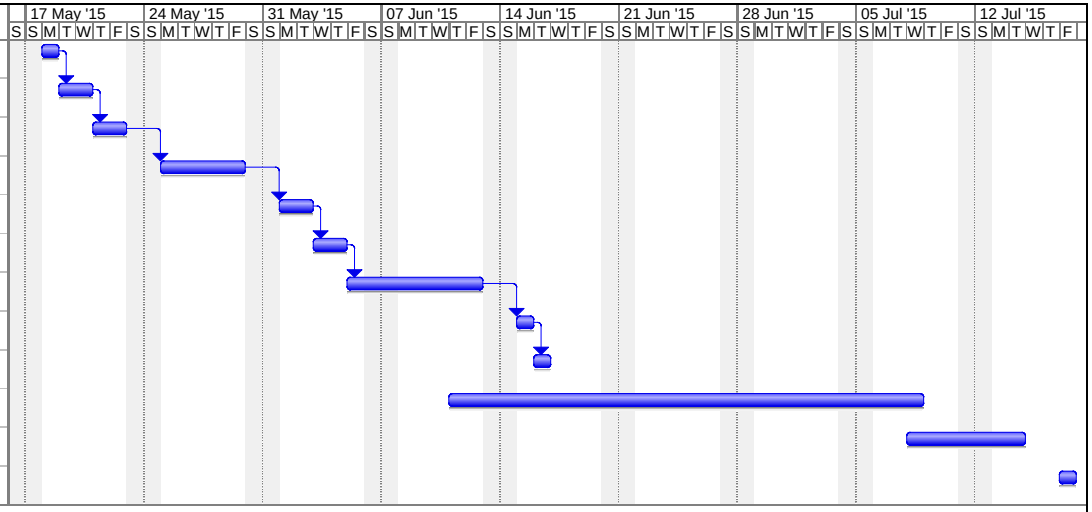

Project: Wellesley Splash Pad 2015 Sc
Date: Tue 05/05/15

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
